
DESTINATION DOWNTOWN CROZET

18 April 2013

CCAC Meeting/Update on Crozet Projects





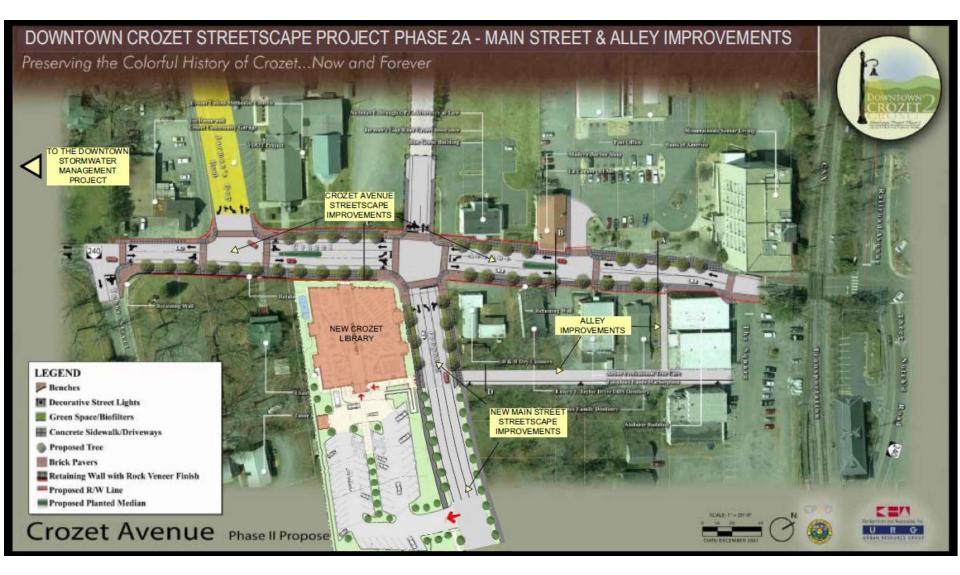

Crozet Library view along Main Street







Library Building:

- ✓ On schedule for a 15 July Substantial Completion
- □ Next Month+ Look ahead (April 2013)
 - □ Complete Dominion power connection
 - □ Start-up HVAC units
 - Complete brick
 - Parking lot grading
 - □ Install sidewalk ramp (switchback)
 - Modification of Library Ave Sidewalk for ADA compliant connection to Lower level (off hours access to lower level)
 - Remaining windows installed by Mid-May
 - Authorize Century Link to move fiber (conflicts with storm sewer)

Storm water Management Project:

 ✓ Final plantings complete, springtime review of vegetation and plantings needed re-seeding (Warranty)





➤ "Streetscape" Project:

Utility Relocation

- Dominion / Comcast
 - Dominion work is approximately 50% complete; Comcast work is 70% complete.
 - Conduits in front of the stores on the square and the new junction box have been installed.
 - Pole installation will be completed in front of the Mud House the week of 4/15/2013.
 - Underground work will start-up again in the next few weeks and is expected to take another few weeks to complete.
 - When Dominion finishes the work at the Tabor St/Crozet Ave intersection the work on Tabor Street will be complete.
 - Work on High Street is complete. They open-cut the road and installed these conduits.
 - Library manhole is being installed in the next week. Installation of conduits to/from the Library has started.





➤ "Streetscape" Project:

Utility Relocation Continued

Dominion / Comcast

- Utility relocation work in the alley is contingent upon the completion of the connection across Claudius Crozet place. Once this work is completed, it will take Dominion another 2 weeks to install their cables and transformers in the alley.
- Overall project should be competed in the next 4 weeks. This does not include taking down the overhead lines or turnover of services to the individual buildings.
- The county will manage individual hook ups and will be coordinating between the contractor (Design Electric) and <u>directly</u> with each affected owner/tenant. This work will begin within the next week to install conduits and meter bases.
- Once Dominion has installed cables to the businesses, it will take approximately 2 week to complete the switchover.
- Once the switchover is completed, Dominion will take another 2 weeks approximately to take down the overhead lines along Crozet Avenue.

• Century Link

- Bids were received and the project has been awarded by Century Link.
- Century Link cannot begin their work until Dominion's contractor has completed their work in The Square anticipated by April 26th.
- The work is expected to last approximately one month.





➤"Streetscape" Project:

- Crozet Ave design Remaining right-of-way/easement dedications:
 - Final Plans & Specs submitted to VDOT; VDOT approval process on-track for June bidding
 - 2 Deeds in process of finalizing for recordation; 1 Deed in process of owner signature. Once recorded we'll submit Right of Way Certification to VDOT and request authorization to Bid.

Over all Milestone Schedule:

- ✓ Submission of Plans/Specs to VDOT for final approval Completed (3/12/13)
- Utility relocation completion May/June
- Recordation of remaining easements April/May
- Revisions/Updates of plans May (if needed)
- Advertise June
- Negotiations/Award to lowest Bidder July/Aug
- Town Hall Meeting With Contractor after awarding (~ July/Aug) to discuss schedule/construction plan
- Notice to Proceed Aug
- Construction ~ 10-12 months depending on phasing





"Crozet North – Safe Routes to School" Project:

Project will provide a "Cross Alert" pedestrian crossing at Crozet Elementary School and new curb and sidewalk on west side of Rte 810 to Ballard Drive.

□ Plans & Specs submitted 2/20/13 to VDOT for final review and approval

□ Right of Way Certification submitted to VDOT

□ VDOT authorization to advertise, then bid project - May

□ Notice to Proceed/Awarding of Contract – July

□ Construction ~ 3 months

CSX Parcel:

✓ Property transfer to the County has been completed.

□ Fence to be installed after the utility relocation work in The Square is complete
